



Directorate of Rural Development

Achievement Report
2025-26

Presented by :
K. Lalrohlua, MCS
DIRECTOR
RURAL DEVELOPMENT

Topics

**Overview of Posts
under RD**

1

Establishment

2

PMKSY

3

PMAY-G

4

SASCI

5

State Priority Programmes

6

Handholding Programme

7

Vibrant Village Programme - II

8

Overview of Posting under Rural Development Directorate

STATUS OF POSTING UNDER DIRECTORATE OF RD, SLMC & IAC, 11-DRD0 & 28-RD BLOCK AS ON 18.05.2026

Sl. No	Name of Office	Asst	IS	EO	UDC	JEO	VLW	LDC	GS	Appr	Total Clerical Staff	JE	Steno	Driver	Rider	Group D	Total Staff
1	Directorate of RD	6	1	0	17	3	0	3	2	2	34	4	1	9	1	19	68
2	SLMC & IAC	0	0	0	1	0	0	0	0	0	1	0	0	1	0	3	5
3	DRDO, Aizawl	0	0	0	1	1	0	3	0	0	5	1	1	1	0	1	9
4	DRDO, Champhai	0	0	0	1	0	0	1	0	0	2	1	1	1	0	2	7
5	DRDO, Hnahthial	0	0	0	0	0	0	1	0	2	3	0	0	1	0	2	6
6	DRDO, Khawzawl	0	0	0	0	0	0	2	0	0	2	0	0	1	0	0	3
7	DRDO, Kolasib	0	0	0	2	0	0	2	0	0	4	0	1	1	0	2	8
8	DRDO, Lawngtlai	0	0	0	1	0	0	2	0	0	3	0	1	1	0	3	8
9	DRDO, Lunglei	0	0	0	0	0	0	2	1	0	3	0	0	1	0	2	6
10	DRDO, Mamit	0	0	0	1	0	0	4	0	0	5	1	1	0	0	3	10
11	DRDO, Saitual	0	0	0	1	0	0	2	0	1	4	0	0	1	0	1	6
12	DRDO, Serchhip	0	0	0	1	0	0	2	0	0	3	0	0	2	0	3	8
13	DRDO, Siaka	0	0	0	0	0	0	2	0	1	3	0	0	2	0	1	6
14	RD Block, Aibawk	0	0	1	1	0	0	1	0	0	3	0	0	0	0	1	4
15	RD Block, Bikhawthlir	0	0	0	1	0	0	2	0	2	5	0	0	1	0	2	8
16	RD Block, Bunglei	0	0	0	0	0	0	1	1	1	3	0	0	1	0	1	5
17	RD Block, Bunglei South	0	0	0	2	0	0	1	0	0	3	0	0	1	0	1	5
18	RD Block, Champhai	1	0	0	2	0	0	0	0	0	3	0	0	1	0	3	7
19	RD Block, Chawngte	0	0	0	1	0	0	1	0	0	2	0	0	1	0	2	5
20	RD Block, Darlawn	0	0	1	0	0	1	2	1	0	5	1	0	0	0	1	7
21	RD Block, East Lungdar	0	0	0	3	0	0	0	0	2	5	1	0	0	0	3	9
22	RD Block, Hnahthial	0	0	0	2	0	1	1	0	0	4	1	0	0	0	3	8
23	RD Block, Kawrtethawveng	0	0	0	0	0	0	2	0	2	4	0	0	0	0	2	6
24	RD Block, Khawbung	0	0	0	2	0	0	2	0	0	4	1	0	0	0	2	7
25	RD Block, Khawzawl	0	0	0	1	0	0	1	0	0	2	0	0	0	0	2	4
26	RD Block, Lawngtlai	1	1	1	1	0	0	0	0	0	4	1	0	1	0	2	8
27	RD Block, Lunglei	1	0	0	1	0	1	0	3	0	6	0	0	0	0	1	7
28	RD Block, Lungsen	0	0	0	0	2	0	1	0	0	3	1	0	0	0	1	5
29	RD Block, Ngopa	0	0	0	1	0	0	1	0	1	3	1	0	0	0	2	6
30	RD Block, Phullen	0	0	0	2	0	0	2	0	1	5	0	0	0	0	1	6
31	RD Block, Reiek	1	0	0	2	0	0	1	0	0	4	0	0	0	0	2	6
32	RD Block, Sangau	0	0	0	0	0	0	1	2	0	3	0	0	0	0	1	4
33	RD Block, Serchhip	0	0	1	2	0	0	0	2	0	5	0	0	0	0	3	8
34	RD Block, Siaka	0	0	0	1	0	0	1	3	0	5	0	0	0	0	2	7
35	RD Block, Thingdawl	1	0	0	0	1	0	0	0	0	2	1	0	1	0	1	5
36	RD Block, Thingsulthliah	0	0	0	1	2	0	1	0	0	4	0	0	0	0	2	6
37	RD Block, Tipa	0	0	0	1	0	0	0	0	0	1	1	0	1	0	1	4
38	RD Block, Tlabung	0	0	0	1	0	0	1	0	2	4	0	0	1	0	1	6
39	RD Block, Tlangnuam	1	0	0	2	1	0	2	1	0	7	1	0	1	0	3	12
40	RD Block, West Phalleng	0	0	0	1	1	0	1	0	0	3	1	0	0	0	1	5
41	RD Block, Zawnuam	0	0	0	2	0	0	1	1	0	4	1	0	0	0	1	6
Total		12	2	4	59	11	3	53	17	17	178	19	6	32	1	90	326

Overview of Posting under Rural Development Directorate

Sl. No	Name of post/grade	Pay Level	No. of Sanctioned Posts	No. of Post filled				Total Filled up post	Vacant
				Dte.	Block	DRDO	SLMC		
1	Director	13	1	1	-	-	-	1	0
2	Joint Director	12	1	1	-	-	-	1	0
3	Deputy Secretary (DWCRD)	12	1	-	-	-	-	0	1
4	Project Director (DRDO)	12	11	-	-	11	-	11	0
5	Project Director (SLMC & IAC)	12	1	-	-	-	1	1	0
6	Dy. Director(General)	11	1	1	-	-	-	1	0
7	Dy. Director(Accts)	11	1	1	-	-	-	1	0
8	Dy. Director(Admn)	11	1	1	-	-	-	1	0
9	Executive Engineer	11	1	1	-	-	-	1	0
10	Project Officer	11	1	1	-	-	-	1	0
11	Dy. Project Director(SLMC & IAC)	11	1	-	-	-	-	0	1
12	Asst. Director(Gen)	10	1	1	-	-	-	1	0
13	Superintendent	10	1	1	-	-	-	1	0
14	Assistant Engineer	10	13	4	-	7	-	11	2
15	Finance & Accounts Officer	10	1	-	-	-	-	0	1
16	Rural Planning Officer	10	1	-	-	-	-	0	1
17	Sr. Scientific Officer	10	1	-	-	-	-	0	1
18	Vety Asst. Surgeon/Veterinary	10	1	-	-	-	-	0	1
19	Steno-I	10	1	-	-	-	-	0	1
20	Statistical Officer (SLMC)	10	1	-	-	-	-	0	1
21	Accounts Officer(SLMC)	10	1	-	-	-	-	0	1
22	AEO/HEO	10	11	-	-	-	-	0	11
23	Block Development Officer	10	28	-	28	-	-	28	0
24	ARDO/AD(RD)/APO	10	15	3	-	8	1	12	3

Overview of Posting under Rural Development Directorate(cont'd)

25	Rural Accounts Officer	10	7	-	-	7	-	7	0
26	Accountant	7	1	-	-	-	-	0	1
27	Assistant/Accountant	7	40	6	6	0	0	12	28
28	EO(Forest)	7	1	-	-	-	-	0	1
29	EO(RD)	7	6	0	4	0	0	4	2
31	I.S	7	35	1	1	0	0	2	33
32	Programme Coordinator	7	1	-	-	-	-	0	1
33	Sr. G/S	7	1	-	-	-	-	0	1
34	Jr. Engineer	7	25	4	12	3	0	19	6
35	Steno-II	7	2	1	-	-	-	1	1
36	EO or Jr EO, AH&V, JEO(Vety)	7	20	-	-	-	-	0	20
37	Steno-III	6	7	-	0	5	0	5	2
38	Asst/Accountant	6	1	-	-	-	-	0	1
39	EO(Indus)	6	1	-	-	-	-	0	1
40	Head Mechanic	6	1	-	-	-	-	0	1
41	JEO(RD)	6	22	3	7	1	0	11	11
42	UDC	6	77	17	33	8	1	59	18
43	VLW	5	15	0	14	0	0	14	1
44	Gram Sevika	4	33	2	14	1	0	17	16
45	Mechanic-II	4	1	-	-	-	-	0	1
46	Soil Demonstrator	4	5	-	-	-	-	0	5
47	Drafman/Tracer	4	2	-	-	-	-	0	2
48	LDC	4	93	3	27	23	0	53	40
49	Driver	2	51	9	8	14	1	32	19
50	Despatch Rider	2	2	1	0	0	0	1	1
51	IV Grade	1	119	19	48	20	3	90	29
TOTAL			666	82	202	108	7	399	267

Establishment Section

Achievement 2025-26

Recruitment & Engagement

- 10 LDCs and 10 Group D recruited
- 13 Casual Drivers have been engaged

Regularization & Upgradation

- 1 LDC(PE) and 1 Group D regularized
- 1 Driver successfully upgraded to a higher grade.
ACP has been implemented for 13 employees.

Promotion & Absorbtion

- 7 LDCs promoted to the post of UDC
- 25 DRDA employees have been absorbed into the Department

e-Office & Kai App

- e-Office successfully implemented w.e.f 1 May,2026
- Use of Kai App implemented since 21.10.2024

Revenue

- Revenue Receipt of Rs 16,86,972/- realised from HRA/License Fee, Room Ren/institutional fee, Guest House Rent out of target of Rs 32 lakhs

Pradhan Mantri Krishi Sinchayee Yojana

Watershed Development Component 2.0



STATE LEVEL NODAL AGENCY : MIZORAM



PMKSY-WDC 2.0
Pradhan Mantri Krishi Sinchayee Yojana-Watershed Development Component



CONFERENCE

Chief Guest : Prof. Lalnilawma, Hon'ble Minister
Rural Development & Administration Department

Venue : AIJAL CLUB, RB McCABE HALL
Date : 06th MAY, 2026, 10:00 AM

Pradhan Mantri Krishi Sinchayee Yojana

Watershed Development Component 2.0



Project Overview

The Pradhan Mantri Krishi Sinchayee Yojana focuses on Watershed and Springshed development in Mizoram.



Status

PMKSY WDC 2.0 is extended to closed on 30th September 2026 & New Version 3.0 likely to start after that.




Achievement

Physical & Financial - Achievement of more than 90% since inception.

Districts/Blockwise Abstract of PMKSY WDC 2.0 Projects taken up during 2021-22

Sl. No.	Name of the District	Name of the Project	Name of Block	No of MWS	Area for treatment (Ha)	Project Cost (in lakh)	Central Share (in lakh)	State Share (in lakh)	Name of PIA	Village Covered
1	Aizawl	Aizawl-I	Darlawn	5	2400	672	604.8	67.2	BDO,Darlawn	Darlawn Chhimveng, N. Serzawl, Sailutar
		Aizawl-II	Thingsuthliah	6	2400	672	604.8	67.2	DRDO,Aizawl	Sesawng, Thingsuthliah
2	Champhai	Champhai-I	Champhai	4	2500	700	630	70	DRDO, Champhai	Ngur, N. Khawbung
		Champhai-II	Khawbung	4	2500	700	630	70	BDO, Khawbung	Farkawn, Khankawn
3	Hnahthial	Hnahthial-I	Hnahthial	4	2400	672	604.8	67.2	DRDO, Hnahthial	Tarpho, Khawhri, S. Chawngtui
4	Khawzawl	Khawzawl-I	Khawzawl	5	2500	700	630	70	DRDO, Khawzawl	Chawngtlai, Tualte
5	Kolasib	Kolasib-I	Thingdawl	4	2500	700	630	70	BDO, Thingdawl	Thingdawl
		Kolasib-II	Bilkhawthlir	4	2500	700	630	70	DRDO, Kolasib	Pangbalkawn
6	Lawngtlai	Lawngtlai-I	Chawngte	8	2500	700	630	70	DRDO, Lawngtlai	Saizawl 'W', Chawngte 'P', Hmunlai, Mualbu 'T'
		Lawngtlai-II	Sangau	10	2500	700	630	70	BDO, Sangau	Lunghzarhtum, Sentetfiang, Siachangkawn, Thaltlang, Vawmbuk
		Lawngtlai-III	Bungtlang S	8	2500	700	630	70	BDO,Bungtlang S.	Hmunnuam, Bungtlang 'S', M. Kawnpui
7	Lunglei	Lunglei-I	Lunglei	4	2500	700	630	70	BDO, Lunglei	Mausen, Haulawng, Mualthuum 'N'
		Lunglei-II	Bunghmun	4	2500	700	630	70	DRDO, Lunglei	S. Lungdai, Serte, Sertlangpui
8	Mamit	Mamit-I	Reiek	4	2500	700	630	70	BDO, Reiek	Reiek, Ailawng
		Mamit-II	Zawnuam	5	2500	700	630	70	DRDO, Mamit	Zawlpui, Zawnuam Vengpui, Thuampui, Bawrai
9	Saiha	Saiha-I	Tipa	3	2500	700	630	70	DRDO, Saiha	Chakhang-I, Chakhang-II, Chakhang-III
10	Saitual	Saitual-I	Ngopa	4	2500	700	630	70	DRDO, Saitual	Hliappui, Pawlrang
11	Serchhip	Serchhip-I	E. Lungdar	4	2400	672	604.8	67.2	DRDO,Serchhip	N. Vanlaiphai, Lungkawih
TOTAL				90	44600	12488	11239.2	1248.8		
Additional Projects (2023-24)										
1	Aizawl	Aizawl-III	Aibawk	3	2500	700	630	70	BDO, Aibawk	Lamchhip, Chawihung, Chamring
2	Kolasib	Kolasib-III	Bilkhawthlir	4	2500	700	630	70	BDO, Bilkhawthlir	Buhchangphai, Phaisen
GRAND TOTAL				97	49600	13888	12499	1388.8		52 Villages

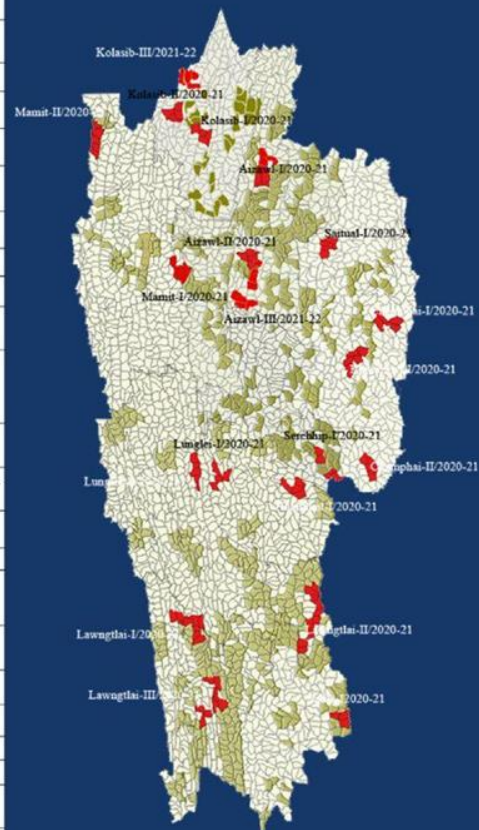

Watershed Map of PMYSY WDC 2.0

PRADHAN MANTRI KRISHI SINCHAYEE YOJANA- WATERSHED DEVELOPMENT COMPONENT 2.0

PROJECT & FUND STATUS

1	No. of projects sanctioned in State	20 Nos
2	Total Area sanctioned in State	49600 ha.
3	Total Project Cost sanctioned	Rs. 13888 Lakhs
4	Total Central Share released by GoI to <u>State</u> till date (since inception)	Rs. 11519.45 Lakhs
5	Total State Share released to <u>SLNA</u> till date (since inception)	Rs. 1279.90 Lakhs
6	Total funds (CS+SMS) received by SLNA till date (since inception)	Rs. 12799.35 Lakhs
7	Total % Fund received till date from Total Project COST (since inception)	Rs. 92.16%

Note : FY 2026-27 allocation is 4.8 Cr out of which Rs 2.4 Cr is already sanctioned from DoLR and is still lying within the State Finance Department .

Cumulative State's Physical Achievement Till Date(MIS Report)

2381.27 Ha	• Area of degraded land covered/Rainfed area developed
6105.10 ha	• Area covered with soil and moisture conservation activities
7696.75 ha	• Area brought under plantation (Afforestation/Horticulture)
1427 nos	• No. of water harvesting structure created/renovated
14094 nos	• No. of farmers benefitted
81 ha	• Area brought under protective irrigation
44398	• No. of man-days generated
535.65 Ha	• Area brought under diversified crops/change in cropping system
459.86 Ha	• Area brought from no crop/single crop to single/multiple crop
1510.44 ha	• Increase in cropped area
16.15%	• Average Increase in farmers' annual income
2753 nos	• No. of Production System Activities Reported
594 nos	• No of Self Help Group Formed (Newly & Existing created)

PMKSY CONFERENCE 6 MAY 2026



PMKSY CONFERENCE 6 MAY 2026

Jan Bhagidari Cup Award





Way forward : PMKSY WDC 3.0

Annexure

Tentative allocation in all the components of WDC 3.0 (Cost Rs. in crore and Area in ha)

Name of the State: Mizoram

Conventional WDC 3.0 projects		Springshed Development:		Funds for completion of ongoing WDC 2.0 projects	Grand Total Cost WDC-PMKSY 3.0
Total Cost	Tentative Area	No. of Springs	Tentative budget		
105.26	37593.49	650	45.5	9.59	160.35

Criteria for selection of project areas in the State/UT

- (i) **Conventional Watershed Projects:** High priority areas in the most vulnerable rainfed and drought prone districts may be selected on the basis of broad criteria given at **Appendix-I**.
- (ii) **Springshed Development:** Suitable and highly potential sites for rejuvenation of springs may be selected as per the criteria given at **Appendix-II**.

Note : PMKSY WDC 2.0 is extended upto 30th September, 2026. So, PMKSY 3.0 preparation is going on and Tentative allocation is already received from DoLR, which will be finalised before closing of PMKSY 2.0

PRADHAN MANTRI AWAAS YOJANA – GRAMIN (Housing For All- Rural)



BRIEF ABOUT THE SCHEME

- Implemented since 1st April, 2016
- Flagship program of the MoRD, Govt. of India
- Aimed at achieving “HOUSING FOR ALL” in rural areas by providing pucca houses with basic amenities to all eligible households.
- Beneficiaries for Financial Years 2016-2021 were selected based on SECC 2011 data and received 4 installments.
- For Financial Years 2021-2022 and 2023-2024, beneficiaries were selected by the system based on Awaas+ 2018 survey data and received in 3 installments.
- SNA-SPARSH fully tested and integrated

PHYSICAL PROGRESS REPORT

Target	29967 (13532 from SECC 2011 & 16435 from Awass+ 2018)
SANCTIONED	29959
COMPLETED	25411
ONGOING/REMAINING	4556

PHYSICAL PERFORMANCE (SECC 2011)

Sl. No.	Financial year	Target	1 st Instalment	2 nd Instalment	3 rd Instalment	4 th Instalment	Completed	Ongoing
1	2016-17	4806	4806	4806	4806	4806	4806	0
2	2017-18	1794	1794	1789	1776	1764	1781	13
3	2019-20	1500	1497	1493	1466	1426	1486	14
4	2020-21	5432	5415	5370	5238	0	5345	87
TOTAL		13532	13512	13458	13286	7996	13418	114

PHYSICAL PERFORMANCE (AWAAS+ 2018)

Sl. No.	Financial year	Target	1 st Instalment	2 nd Instalment	3 rd Instalment	Completed	Ongoing
1	2021-22	6976	6941	6780	6426	6610	366
2	2023-24	9459	7263	5725	3574	5383	4076
TOTAL		16435	14204	12505	1000	11993	4442

AWAAS+ 2024 SURVEY

Total Survey	54601
SELF SURVEY	140
ASSISTED SURVEY	54461
TOTAL ACCEPTED CASES	45604
TOTAL DISPUTED CASES	8997



ISSUES & CHALLENGES

- Delays in the release of installments from the state or central government can halt construction progress, leaving beneficiaries stranded with incomplete houses.
- The fixed financial assistance provided under the scheme is often insufficient to cover the complete cost of constructing a house, especially given rising prices.
- The high cost and limited availability of construction materials, particularly in remote areas, significantly inflate the overall project expenses.
- Difficult Terrain and Remote Locations: Mizoram's hilly topography and scattered, remote villages make transportation of construction materials extremely difficult, time-consuming, and expensive. Many sites are not easily accessible by road.
- Mizoram is prone to landslides, especially during the monsoon season. This can damage incomplete structures, delay construction, and require additional funds for site stabilization or repairs.

5 SPECIAL ASSISTANCE TO STATES FOR CAPITAL INVESTMENT(SASCI)




**FLAGGING OFF BOOKS FOR
LIBRARIES
UNDER SASCI - PART VII**

ESTABLISHMENT OF NEW LIBRARIES IN MIZORAM

PROJECT COST : RS 55.18 CR

(Rs in Cr)			
1	Construction of Library Building (Civil work)	34.49	Completed
2	Electrification	3.69	Completed
3	Procurement of Books from Local Market	2.73	Completed
4	Procurement of Books from NBT, India	2.73	Work in progress
5	Procurement of Computers, 3KVA Power back up, Reading Table, Bookshelves , Quality control, Contingencies, Administrative Cost etc	11.14	Work in progress
6	Labour Cess	0.38	Completed



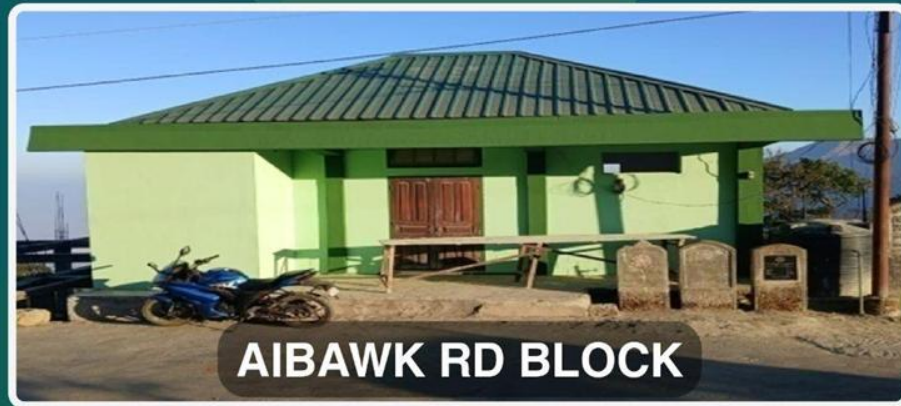



SCHEME COMPONENTS

- Computer sets
- Printer
- LED TV
- 3kva power backuP
- Books & bookshelves

UPCOMING SASCI PROJECT

1. NAME OF PROJECT : CONSTRUCTION OF KHAWKUNGA HALL AT N. BUKPUI
2. PROJECT COST : RS. 2.70 CR.
3. BUDGETARY ALLOCATION AND AA OBTAINED.
4. DPR UNDER PREPARATION.



STATE PRIORITY PROGRAMME(SPP)

Sl No	Particulars	No. of Works	Amount (Rs in lakh)	Status
1	Works under Mamit Dist.	47	204	Completed
2	Works under Lawngtlai Dist.	140	730	Completed
3	Works under Serchhip Dist.	2	15	Completed
4	Works under Champhai Dist.	3	52	Completed
5	Works under Saitual Dist.	1	5	Completed
6	Works under Kolasib Dist.	1	20	Completed

**Futsal Ground
Thingdawl
Rs 20,00,000/-**



HANDHOLDING PROGRAMME 2025-26

Sl No	Name of Works	No. of Works	Amount (Rs in lakh)	Status
1	Works under Mamit Dist.	2	100	Completed
2	Works under Khawzawl Dist.	1	38.73	Completed
3	Works under Aizawl Dist.	1	32.7	Completed
4	Works under Champhai Dist.	3	10	Completed
5	Works under Serchhip Dist.	2	21	Completed
6	Works under Lunglei Dist.	1	50	Work in progress
		10	252.43	



YMA HALL, PHAI VENG, CHAWNGTLAI, AMOUNT = 38.73 LAKH



VIBRANT VILLAGES PROGRAMME – II(VVP-II)


(2024-25 to 2028-29)

9. VIBRANT VILLAGES PROGRAMME – II (VVP-II) 2024-2028



- **Implemented by Department of Border Management, Ministry of Home Affairs at Central Level**
- **The scheme aims at holistic development of strategic border villages through ; Infrastructure, Livelihood generation, Connectivity, Tourism, Education, Security integration**
- **VVP-II is a Center Sector Scheme 100% Funded by the Government of India**
- **Financial Outlay for each village is Rs 3.00 Cr**
- **Mizoram has a total of 109 identified villages in 16 RD Blocks under VVP-II**
- **Expected Total Financial Outlay for Mizoram is Rs Rs 327.00 Cr**
- **Admin Fund of Rs 2 lacs per village will be earmarked for each village for the entire programme period.**

VVP-II RD Blocks

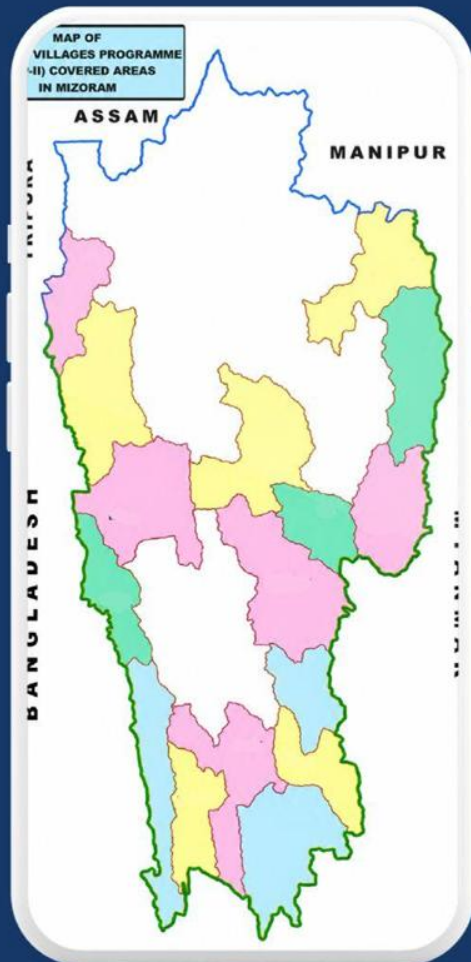

1. Ngopa RD Block
2. Champhai RD Block
3. Khawbung RD Block
4. E. Lungdar RD Block
5. Hnahthial RD Block
6. Bunghmun RD Block
7. Siaha RD Block
8. Tipa RD Block
9. Sangau RD Block
10. Lawngtlai RD Block
11. Bungtlang 'S' RD Block
12. Chawngte RD Block
13. W. Phaileng RD Block
14. Kawrtethawveng RD Block
15. Tlabung RD Block
16. Serchhip RD Block





Intervention Area	Sub-Category
Development of Co-operative, SHGs and FPOs for managing livelihood opportunities and maintenance fo assets created under programme	Development and capacity building of co-operative societies/SHGs/FPOs.
Education Infrastructure	1. Higher Secondary School infrastrucutur 2. Pre-School/Anganwadi/balwadi 3. Primary School infrastructure 4. Secondary School infrastrcuture 5. Smart classrooms
Empowerment of Youth and Skill Development	1. Skilling-related infrastructure 2. Skilling activities
Energization	1. Off-grid electrification (Small/Mini/Micro Hydel System,solar home lighting system etc) 2. On-grid electrification (substation, HT/LT Line, augmentation etc) 3. Other renewable solutions 4. Solar street lights/High mast 5. Solar water heating system



Intervention Area	Sub-Category
Promotion of Tourism and Culture Outreach Activities	1. Fairs and festivals 2. Outreach and awareness programmes 3. Promotion of culture 4. Tourism-related infrastructure like wayside amenities, tourist facilitation centre etc 5. Trek routes/Adventure tourism
Road Connectivity	1. Bridges/FSBs 2. Road Project, including bridges
Television and Telecom connectivity	Related Infrastructure
Village infrastructure including health facilities	1. CHC/HWC/PHC/SHC 2. Common Service Centre (CSC) 3. Drinking water supply and distribution 4. Eco-regeneration works 5. Flood Protection Works 6. Housing 7. Irrigation works 8. Market infrastructure 9. Mobile Medical Unit/Ambulance 10. Multipurpose Community Hall 11. Sanitation, drains and waste management 12. Sports infrastructure 13. Telemedicine 14. Veterinary aid services 15. Village internal connectivity infrastructure

CURRENT STATUS

Particular	Nos of Village	Profile Update	Verified
Identified Village	109	109	109
Saturation Village	566	285	435

DISTRICT LEVEL COMMITTEE, SERCHHIP HAS SUBMITTED 13 NOS OF VILLAGE ACTION PLAN THROUGH VVP PORTAL AND IS UNDER REVIEW/SCRUTINY

VILLAGE ACTION PLAN FROM OTHER DISTRICTS ARE BEING AWAITED

INSTITUTIONAL FRAMEWORK FOR VVP-II IMPLEMENTATION

CENTRAL GOVERNMENT LEVEL



STATE GOVERNMENT LEVEL



DISTRICT LEVEL

- Department of Border Management, Ministry of Home Affairs is the Nodal Department
 - Project Screening Committee is constituted under the Chairmanship of Joint Secretary with representatives from concerned Ministry/Department
-

- RD & AD is the Nodal Department
 - Commissioner/Secretary RD & AD is the Nodal Officer and Director, RD Directorate is the Asst Nodal Officer
 - State Level Screening Committee is constituted under the Chairmanship of Chief Secretary with representatives of Line Departments.
-

- A District Level Committee is constituted under the Chairmanship of District Magistrate / Deputy Commissioner
 - Line Departments are also included.
-



THANK YOU

